


DDMT MONITORING WELL INSTALLATION DIAGRAM (FLUSH MOUNT COMPLETION)			
PROJECT NAME:	DDMT	PROJECT NO.	6301-04-0002
WELL ID.	MW-145	NORTHING:	280967.63 EASTING: 800823.18
DATE	06/03/04	START TIME	17:00
GROUND SURFACE ELEVATION: 284.86 BENTONITE TYPE 3/8" Coarse Grade			
		MANUFACTURER Bariod	
TOP OF SCREEN ELEVATION: 208.44		CEMENT TYPE Type II Portland Cement	
		MANUFACTURER LoneStar	
REFERENCE POINT ELEVATION 284.72		BOREHOLE DIAMETER 6"	
		MACTEC FIELD REPRESENTATIVE Amy Callaway	
TYPE FILTER PACK 20/40 Sand		DRILLING CONTRACTOR ProSonic	
FILTER PACK MANUFACTURER FilterSil		AMOUNT BENTONITE BELOW (SCREEN) 2 bags (50 lb)	
		AMOUNT BENTONITE USED (SEAL) 2 bag (50 lb)	
SCREEN MATERIAL Schedule 40 PVC		AMOUNT BENTONITE USED (GROUT) 10 lbs	
MANUFACTURER Johnson		DENSITY OF GROUT 13.7 lbs/kg	
		13.5 lbs/kg	
RISER DIAMETER 2"		AMOUNT CEMENT USED (GROUT) 8 bags (94 lb)	
DRILLING TECHNIQUE Rotasonic		AMOUNT SAND USED 8.5 bags (50 lb)	
AUGER/BIT SIZE AND TYPE 6"/2"			
		STATIC WATER LEVEL (>24 hrs after dev) 69.02	
REMARKS		MEASURED ON (Date/Time) 6/24/2004	

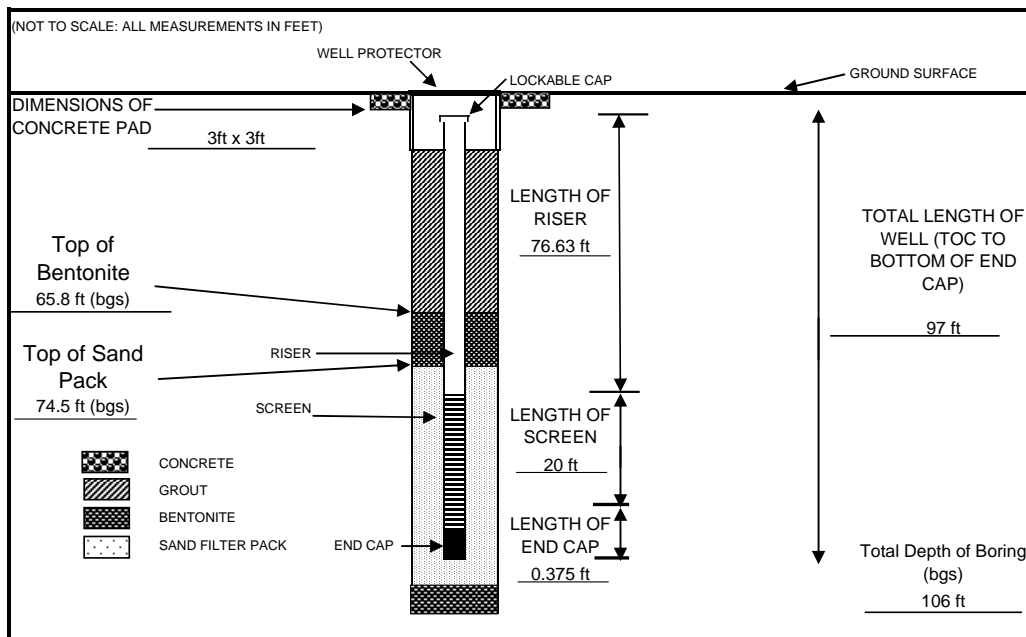

QA / QC	DRILLER: David Wilcox	INSPECTOR: Amy Callaway
	DISCREPANCIES:	CHECKED BY: RNQ DATE: 09/03/04
