

Adams
6/3/93

C993C207

STATUS REPORT

2 June 1993

STUDY NAME: East End Dauphin Island, Alabama, and Dauphin Island Shoreline, Alabama, Section 14 Studies

STUDY MANAGER: Walt Burdin

TELEPHONE: 690-2772

STUDY AUTHORITY: Section 14 of the 1946 Flood Control Act

GENERAL DESCRIPTION OF STUDY: There is a severe erosion problem at two separate locations on Dauphin Island. One is at Fort Gaines, on the east end of the island, and the other is at the Main Beach Park, a public park with a fishing pier, which is about 3 miles west of Fort Gaines. The Dauphin Island Park and Beach Board (DIPBB) requested that the Corps investigate these problems and recommend a feasible solution.

WORK COMPLETED LAST MONTH: Feasible alternatives were developed for both study sites. The DIPBB sent us Letters of Intent on both proposed projects. The final DPR on East End Dauphin Island was submitted late in April 1993. The final DPR on Dauphin Island Shoreline was submitted in mid-May 1993. Informal SAD review comments on the East End DPR have been minor. No comments have yet been received on the DI Shoreline DPR. ADECA was to provide funds for the local share of the cost on the DI Shoreline project. These funds were inadvertently omitted from the ADECA appropriations submittal and their status is presently indefinite.

WORK SCHEDULED NEXT MONTH: Clarify status of local funds for both projects. SAD will require firm information when the request for construction funds is submitted to HQUSACE.

MILESTONE/SCHEDULE SUMMARY:

	<u>Scheduled</u>	<u>Revised</u>	<u>Accomplished</u>
Initiate Studies	7/92		7/92
Evaluate Alternatives	9/92		10/92
Prepare Draft Reports	10/92		10/92
Complete Inhouse Review	11/92	3/93	4/93
Submit Feasibility Reports	12/92	4/93	5-5/93

ITEMS REQUIRING ATTENTION: There has been some adverse publicity

concerning the proposed "rock on the beach" work under the Dauphin Island Shoreline. We are working on a public involvement plan which will hopefully counter much of this. I have been invited to attend a meeting of the East End Committee Friday, 4 June 1993. Depending on the results of that meeting, and allowing for other local factors, we will initiate additional meetings as soon possible.

FUNDS: Thru March 1992


TOTAL AVAILABLE FOR OBL.	\$ 57,672		<u>OBL.</u>	<u>EXP.</u>
OBLIGATED TO DATE	\$ 57,672	SCH.	\$ 57,672	\$ 57,672
UNOBLIGATED BALANCE	\$ 0	ACT.	\$ 57,672	\$ 57,672

LAST STUDY TEAM MEETING: 8 February 1993

PURPOSE AND RESULTS OF MEETING: A formal meeting was not held. However, all team members were sent "team review" drafts of the reports. The inhouse review drafts were prepared using the comments from the team.

STUDY TEAM MEMBERS:

<u>TEAM MEMBER</u>	<u>OFFICE</u>	<u>TELEPHONE</u>	<u>ATTENDED LAST MEETING (*)</u>
Joe Ellsworth	EN-EC	3751	
Ray Gustin	EN-FS	2685	
Greg Miller	EN-YD	4010	
Kim Blum	PD-FE	3884	
Doug Nester	PD-EC	3854	
Kevin McCauley	RE-P	2560	
Ashford Kettler	RE-A	3298	
Vernon Holmes	EN	3440	

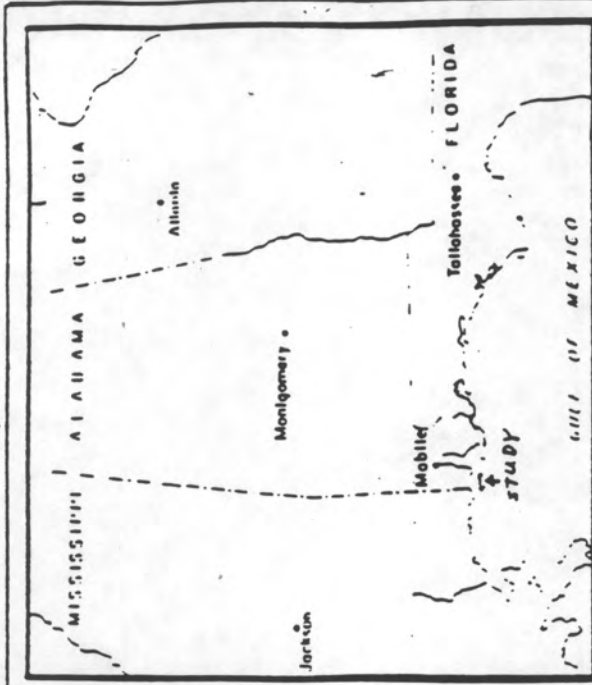

EAST END DAUPHIN ISLAND AND
DAUPHIN ISLAND SHORELINE

SECTION 14



US Army Corps
of Engineers
Mobile District

