

BLACK WARRIOR/TOMBIGBEE RIVER: DEMOPOLIS LOCK – UPPER MITER SILL FAILURE – 6 FEB 2024

6 February 2024 condition update:

The District Fleet arrived at Demopolis Lock on Friday (2/2) evening. Saturday (2/3) morning, fleet components were positioned to assist with lifting the stoplogs and place support machinery and equipment for the upcoming work. The upper stoplogs were cracked open to fill the chamber and allow the fleet to reposition.

On Monday (2/5) and Tuesday (2/6), the upper stoplogs were restacked to elevation 84.0, giving more protection from upper pool fluctuations.


District Engineering has finalized the plans & specifications for the sill repair. The modification to the O&M contract should be awarded this week.



Damaged Sill



District Fleet Downstream
for Debris Removal

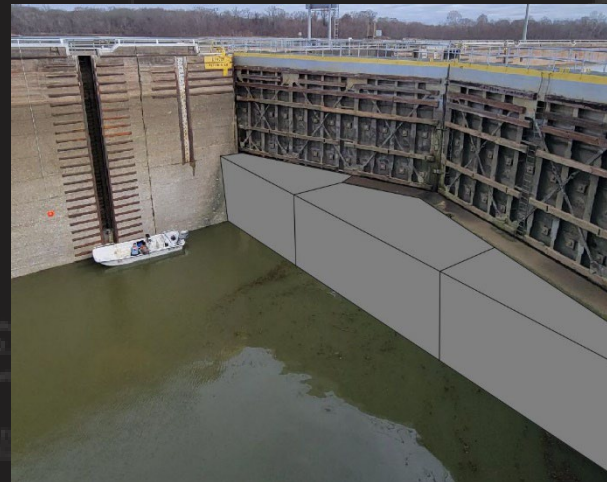

Rendering of Repair



Fleet Positioning for
Upcoming Work



US Army Corps
of Engineers®

U.S. ARMY

BLACK WARRIOR/TOMBIGBEE RIVER: DEMOPOLIS LOCK – UPPER MITER SILL FAILURE – 20 JAN 2024

20 January 2024 condition update:
At 0700, District Crisis Team held a safety and coordination meeting with TVA, R&D Maintenance, and Specialty Diving, Inc. to go over safety hazards, the dive plan, and the plan and procedures for lifting and placing the stoplogs. By 0800, all details and safety plans were finalized, and the team began operations.


The team experienced delays due to frozen air lines in the latching device on the picking beam. At 1100, TVA vessel Freedom began moving three stoplogs (RG3, RG4, and SP2) from the esplanade onto the TTWW stoplog barge. Complete at 1230.

At 1300, the dive team inspected the stoplog slot. No issues were found.

At 1330, TVA began setting 5 stoplogs (1 heavy, 2 regular BWT, 2 regular TTWW). Last stoplog was set at 1700.



Diver Inspecting Stoplog Slot

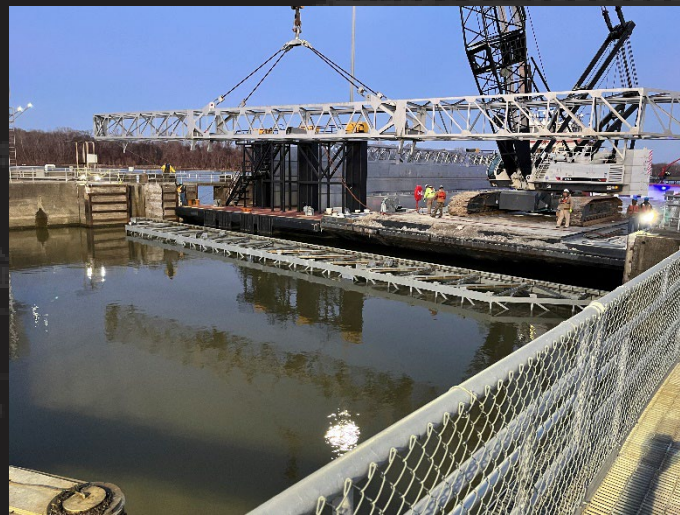

Setting Stoplogs

Last Stoplog Set




GOAL 2

Deliver Integrated Water Resource Solutions



US Army Corps of Engineers®

U.S. ARMY

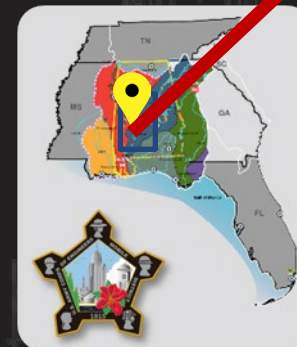

BLACK WARRIOR/TOMBIGBEE RIVER: DEMOPOLIS LOCK – UPPER MITER SILL FAILURE - 19 JAN 2024

19 January 2024 condition update:
At 0700 District Crisis Team held a coordination meeting with Parker Towing to go over the lower miter gate closing plan. By 1030 all details and safety plans were finalized, and the team began operations.

Parker Towing placed barges in the chamber and arrange their 3 towboats and additional barges downstream of the miter gates by 1115.

The lower miter gates were moved out of recess at 1130 and, following the gate closing procedure, were successfully placed into mitered position by 1145.

The lock chamber was filled and the head on the upper gates were equalized stopping the uncontrolled flow by 1220.


TVA vessel FREEDOM will arrive at 2100, 19 JAN, with crane barge and addition stoplogs from the Tenn-Tom Waterway. Upper stoplog setting operations will begin at 0700, 20 JAN.



Lower Miter Gates Closed



Lower Miter Gates Closing

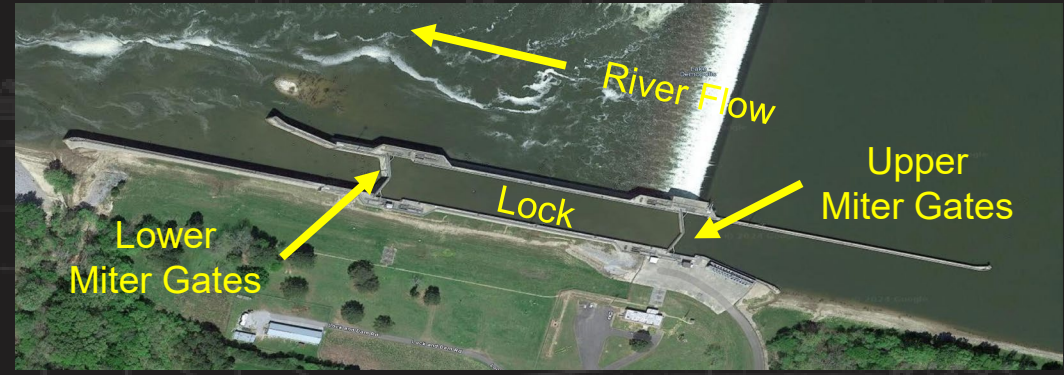

GOAL 2

Deliver Integrated Water Resource Solutions



U.S. ARMY



US Army Corps of Engineers®





BLACK WARRIOR/TOMBIGBEE RIVER: DEMOPOLIS LOCK – UPPER MITER SILL FAILURE - 16 JAN 2024

16 January 2024 Incident:
At 0600 the on-duty lock operator heard a loud noise and while investigating noticed water flowing under the upper miter gate. The concrete that comprises the upper miter sill fractured, allowing water to pass under the gate. The lower lock gates were open at time of the incident.

Project contacted District personnel to start planning courses of action. Notice to Mariners are being issued to update users.

Current operations are to close the lower miter gates to allow the pool to equalize and set the upper stoplogs to get the lock chamber under control. Operation will take place 19-21 January. Engineering and Operations are continuing to analyze the extent of damages and are working other courses of action to stop the flow and get the lock under control.

At this time, the extent of damages have not been determined. Once the lock is dewatered damage assessment and repair plans can be developed. No accurate estimate for closure duration is available at this time. This schedule will be refined once a full assessment of the damages can be performed.

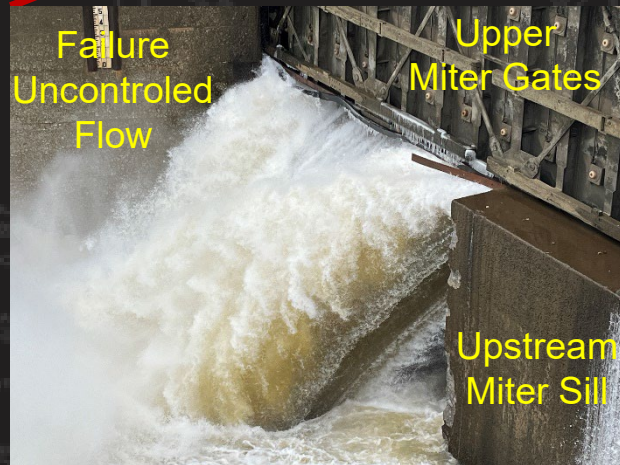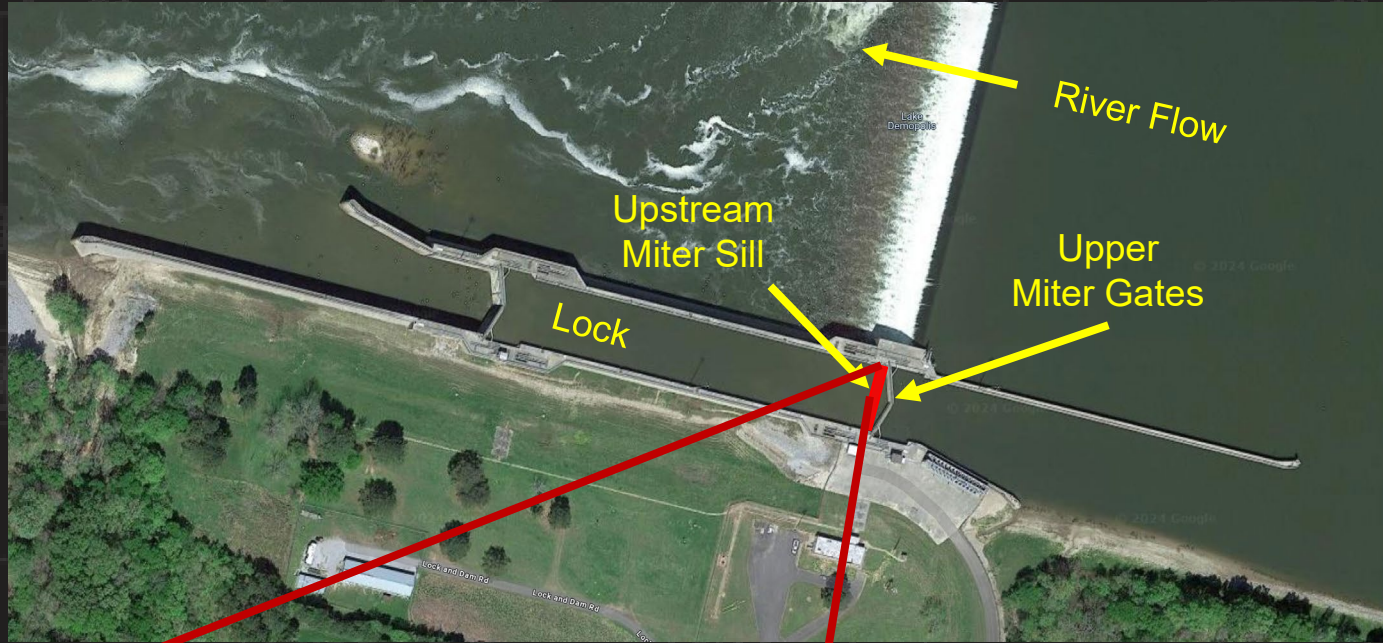

GOAL 2
*Deliver Integrated
Water Resource
Solutions*



**US Army Corps
of Engineers®**

U.S. ARMY
