


DDMT MONITORING WELL INSTALLATION DIAGRAM (FLUSH MOUNT COMPLETION)

PROJECT NAME: <u>DDMT</u>	PROJECT NO. <u>6301-04-0002</u>
WELL ID. <u>MW-160</u>	NORTHING: <u>281366.52</u> EASTING: <u>801304.26</u>
DATE <u>10/11/04</u>	START TIME <u>12:45</u>

GROUND SURFACE ELEVATION: <u>294.11</u>	BENTONITE TYPE <u>3/8" Coarse Grade</u>
TOP OF SCREEN ELEVATION: <u>228.30</u>	MANUFACTURER <u>Bariod</u>
REFERENCE POINT ELEVATION <u>294</u>	CEMENT TYPE <u>Type II Portland Cement</u>
	MANUFACTURER <u>LoneStar</u>
TYPE FILTER PACK <u>20/40 Sand</u>	BOREHOLE DIAMETER <u>6"</u>
FILTER PACK MANUFACTURER <u>FilterSil</u>	MACTEC FIELD REPRESENTATIVE <u>Kevin Arnold</u>
SCREEN MATERIAL <u>Schedule 40 PVC</u>	DRILLING CONTRACTOR <u>ProSonic</u>
MANUFACTURER <u>Johnson</u>	AMOUNT BENTONITE BELOW (SCREEN) <u>2 (5 gallon) buckets</u>
	AMOUNT BENTONITE USED (SEAL) <u>1 (5 gallon) buckets</u>
	AMOUNT BENTONITE USED (GROUT) <u>3/4 bucket</u>
	DENSITY OF GROUT <u>13.5 lbs/kg</u>
	<u>13.6 lbs/kg</u>
RISER DIAMETER <u>2"</u>	
	AMOUNT CEMENT USED (GROUT) <u>8 bags (94 lb)</u>
DRILLING TECHNIQUE <u>Rotosonic</u>	AMOUNT SAND USED <u>7.5 bags (50 lb)</u>
AUGER/BIT SIZE AND TYPE <u>6"/4"</u>	
	STATIC WATER LEVEL (>24 hrs after dev) <u>79.19</u>
REMARKS _____	MEASURED ON (Date/Time) <u>10/6/2004</u>

(NOT TO SCALE: ALL MEASUREMENTS IN FEET)

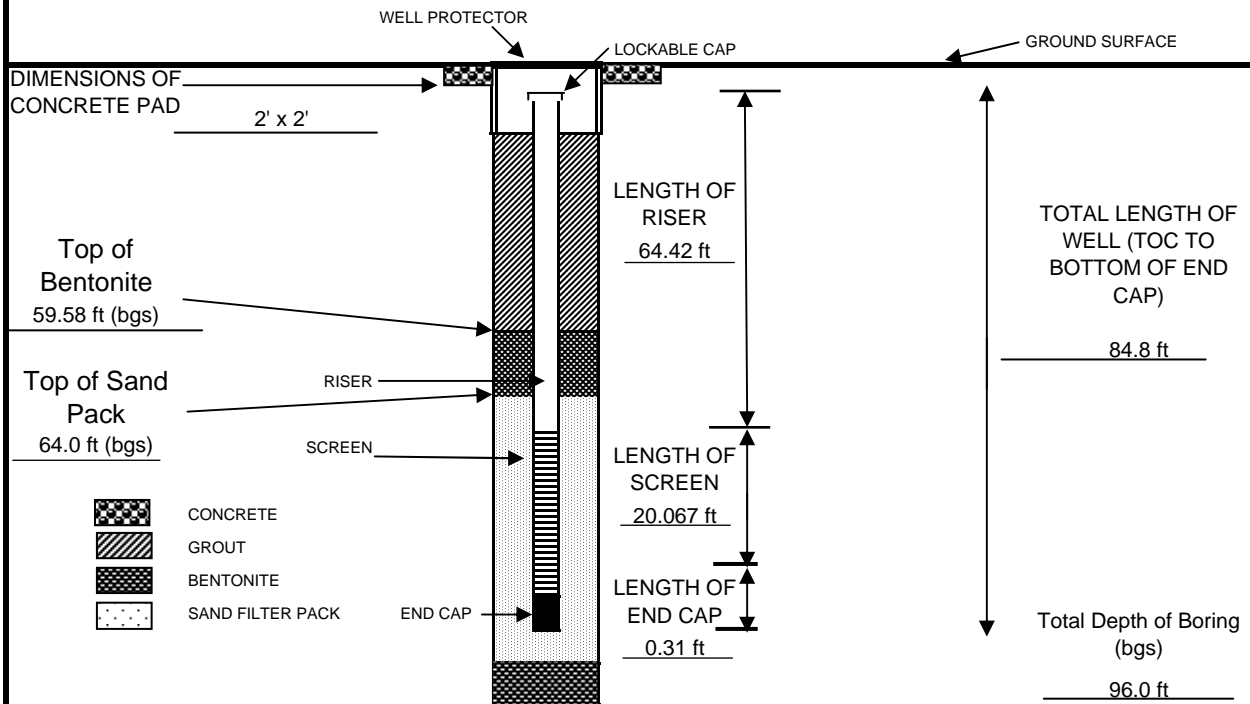

QA / QC

DRILLER: David Wilcox INSPECTOR: Kevin Arnold
 DISCREPANCIES: _____ CHECKED BY: RNQ DATE: 11/19/04
