




PROJECT NUMBER	177556.SA.FE	WELL NUMBER	MW-186	SHEET 1 OF 1
WELL COMPLETION DIAGRAM				

PROJECT : DDMT 2005 Well Installation LOCATION : Memphis Depot, Dunn Field

DRILLING CONTRACTOR Prosonic Corp

DRILLING METHOD AND EQUIPMENT USED Rotasonic rig (4 inch sample casing / 6 inch outer casing)

WATER LEVELS : START : 10/31/2005 END: 10/31/2005 LOGGER : Mike Karafa

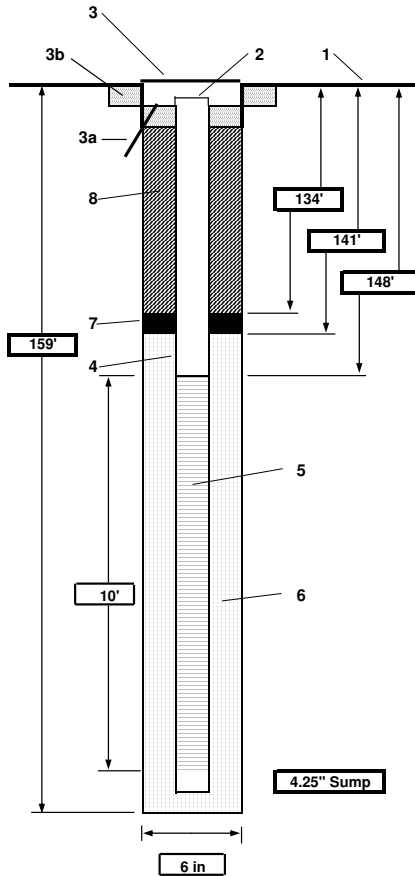

Note: Diagram not to scale.
Back filled boring from 186' to 159' with bentonite chips

1- Ground elevation at well	256.69 feet MSL
2- Top of casing elevation	256.31 feet MSL
3- Wellhead protection cover type	Flush-mount wellhead pad
a) drain tube?	No
b) concrete pad dimensions	3 by 3 feet
4- Dia./type of well casing	2" ID Sch 40 PVC
5- Type/slot size of screen	2" ID Sch 40 PVC 0.010 in slotted screen
6- Type screen filter	Unimin FilterSil 20/40 #00N
a) Quantity used	Unspecified bags
7- Type of seal	Pure Gold Medium Bentonite Chips
a) Quantity used	Unspecified bags
8- Grout	
a) Grout mix used	Loanstar Type I/II Portland Cement and bentonite powder 12.1 lbs
b) Method of placement	Tremmie Method
c) Vol. of well casing grout	
Development method	Grundfos surge and develop with YSI
Development time	2.75 hour
Estimated purge volume	550 gallons
Comments	Depth To Water (DTW) = 83.58 feet
Final field parameters collected during well development (11/9/05):	
pH =	6.16
conductivity =	0.510 mS/cm
temperature =	18.85 °C
Dissolved Oxygen =	4.67 mg/l
Turbidity =	5.7 NTU
