


US ARMY ENVIRONMENTAL HYGIENE AGENCY
TABLE 2 - GROUNDWATER MONITOR WELL SUMMARY

PROJECT 38-26-0195-82 DATE 6 JULY 82
DDMT

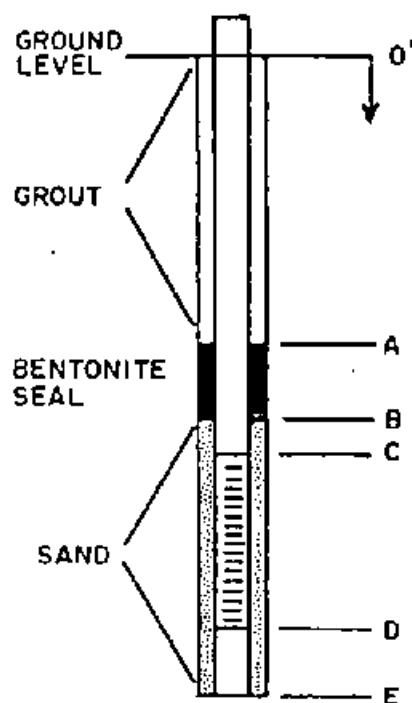

A - TOP OF BENTONITE SEAL
B - TOP OF SAND
C - TOP OF WELL SCREEN
D - TOP OF SEDIMENT TRAP
E - TOTAL WELL DEPTH

WELL NO.	MW 1	MW 2	MW 3	MW 4	MW 5	MW 6	MW 7
A		9'-6"	60'-0"	3'-0"	54'-0"	30'-0"	49'-0"
B		13'-0"	63'-0"	3'-0"	57'-0"	33'-0"	54'-0"
C		18'-0"	63'-6"	58'-6"	57'-0"	50'-0"	64'-0"
D		32'-0"	73'-6"	78'-6"	77'-0"	70'-0"	74'-0"
E		32'-0"	73'-6"	78'-6"	77'-0"	70'-0"	74'-0"
GROUT THICKNESS		9'-6"	15'-0"	3'-0"	15'-0"	9'-0"	15'-0"
BENTONITE SEAL THICKNESS		3'-6"	3'-0"	0	3'-0"	3'-0"	5'-0"
LENGTH OF PIPE	72'-2"	20.0'	65'-6"	60'-0'	60'-0"	51'-0"	67'-0"
LENGTH OF STANDPIPE		2'	2'	1'-6"	3'	1'	3'
LENGTH OF SCREEN	10'	10'	10'	20'	20'	20'	10'
LENGTH OF SEDIMENT TRAP	0	0	0	0	0	0	0
SCREEN (In.) SLOT SIZE	0.010	0.010	0.010	0.010	0.010	0.010	0.010
INITIAL (ft.) WATER LEVEL	N/A	274'-3"	228'-5"	230'-4"	228'-6"	229'-7"	231'-6"
24 HOUR (ft.) WATER LEVEL	N/A	269'-5"	228'-10"	230'-3"	228'-6"	229'-1"	231'-1"
GROUND LEVEL ELEVATION ft.		289'-8"	290'-5"	300'-0"	301'-4"	288'-1"	293'-1"
REMARKS							
Completion Date	casing broken 24 JUNE	24 JUNE	26 JUNE	26 JUNE	27 JUNE	29 JUNE	29 JUNE
