



WELL INSTALLATION DIAGRAM

WELL NO.: MW-208B

PROJECT: DDMT - Phase 2 Wells

PROJECT NUMBER: 3202-019

SITE LOCATION: MI

e2M PROJECT MANAGER: T. Holmes

e2M FIELD STAFF: Jim Anstaett

DATE COMPLETED: 3/24/07

WELL LOCATION: 60 ft. northeast of curb at intersection of W.E. Freeman and Memphis Deppot Pkwy.

NORTHING: 277396.9

EASTING: 802814.96

GROUND SURFACE ELEVATION (ft, msl): 302.08

TOP OF CASING ELEVATION (ft, msl): 301.79

TOP OF SCREEN ELEVATION (ft, msl): 195.1

DRILLING CO.: Prosonic

DRILLING METHOD: Sonic

BOREHOLE DIAMETER (in): 6

SURFACE COMPLETION: Flush Mount

BOLLARDS: No

WELL DIAMETER (in): 2

TYPE OF SCREEN/RISER MATERIAL: PVC Schedule 40

SLOT SIZE OF SCREEN: 0.010

TYPE OF FILTER PACK: Sand

GRADATION OF FILTER PACK: 10-20

QUANTITY OF FILTER PACK: 7-50lb. Bags

TYPE OF BENTONITE IN SEAL: 3/8" Shur Plug Chips

QUANTITY OF BENTONITE IN SEAL: 2-50lb. Bag

TYPE OF GROUT: Portland Type I

QUANTITY OF GROUT: 18-94lb. Bags


DEVELOPMENT METHOD: Grundfos RediFlow II

DATE DEVELOPED: 4/3/2007

DEPTH TO WATER (ft.btoc): 105.42-ft. - 5/4/2007

NOTES:

**Well
Completion
(Not to Scale)**

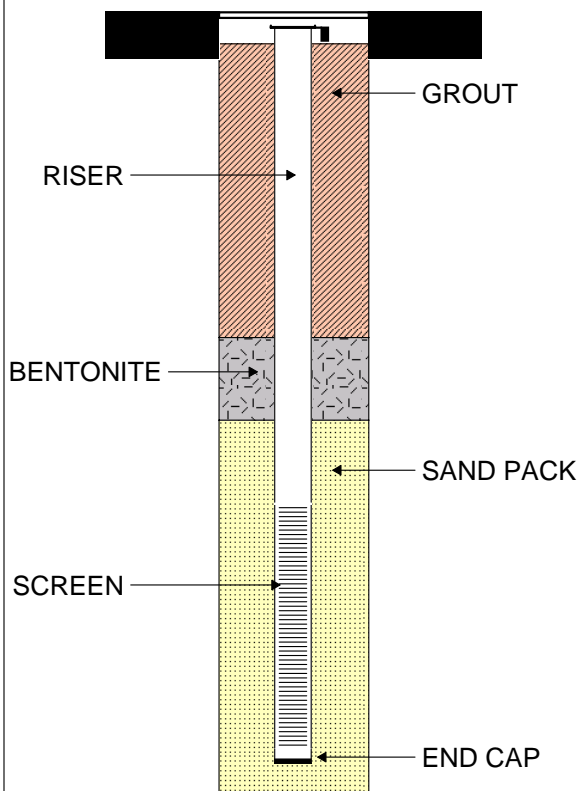

**Well
Details**

DIMENSIONS OF CONCRETE PAD: 3-ft. by 3-ft.

LENGTH OF RISER (ft): 106.7

DEPTH TO TOP OF BENTONITE (ft, bgs): 94

DEPTH TO TOP OF SAND PACK (ft, bgs): 100

LENGTH OF SCREEN (ft): 15

LENGTH OF END CAP: 0.3

TOTAL DEPTH OF WELL (ft, btoc): 122

DEPTH TO TOP OF BACKFILL (ft, bgs): NA

TOTAL DEPTH OF BORING (ft, bgs): 126

Prepared by: **WTR**

Date: **5/16/2007**

Checked by: **KMS**

Date: **5/16/2007**
