



WELL INSTALLATION DIAGRAM

WELL NO.: MW-210A


PROJECT: DDMT - Phase 2 Wells
 PROJECT NUMBER: 3202-019
 SITE LOCATION: MI
 e2M PROJECT MANAGER: T. Holmes
 e2M FIELD STAFF: Jim Anstaett
 DATE COMPLETED: 4/19/07
 WELL LOCATION: 190 ft. south of Bldg. 865.

NORTHING: 277238.49
 EASTING: 801958.05
 GROUND SURFACE ELEVATION (ft, msl): 289.78
 TOP OF CASING ELEVATION (ft, msl): 289.66
 TOP OF SCREEN ELEVATION (ft, msl): 112.6

DRILLING CO.: Prosonic
 DRILLING METHOD: Sonic
 BOREHOLE DIAMETER (in): 6
 SURFACE COMPLETION: Flush Mount
 BOLLARDS: No
 WELL DIAMETER (in): 2
 TYPE OF SCREEN/RISER MATERIAL: PVC Schedule 40
 SLOT SIZE OF SCREEN: 0.010

TYPE OF FILTER PACK: Sand
 GRADATION OF FILTER PACK: 10-20
 QUANTITY OF FILTER PACK: 12.5-50lb. Bags
 TYPE OF BENTONITE IN SEAL: 3/8" Shur Plug Chips
 QUANTITY OF BENTONITE IN SEAL: 5.5-50lb. Bag
 TYPE OF GROUT: Portland Type I
 QUANTITY OF GROUT: 40-94lb. Bags
 DEVELOPMENT METHOD: Grundfos RediFlow II
 DATE DEVELOPED: 4/24/07-4/25/07
 DEPTH TO WATER (ft.btoc): 98.31-ft. - 5/4/2007

NOTES:

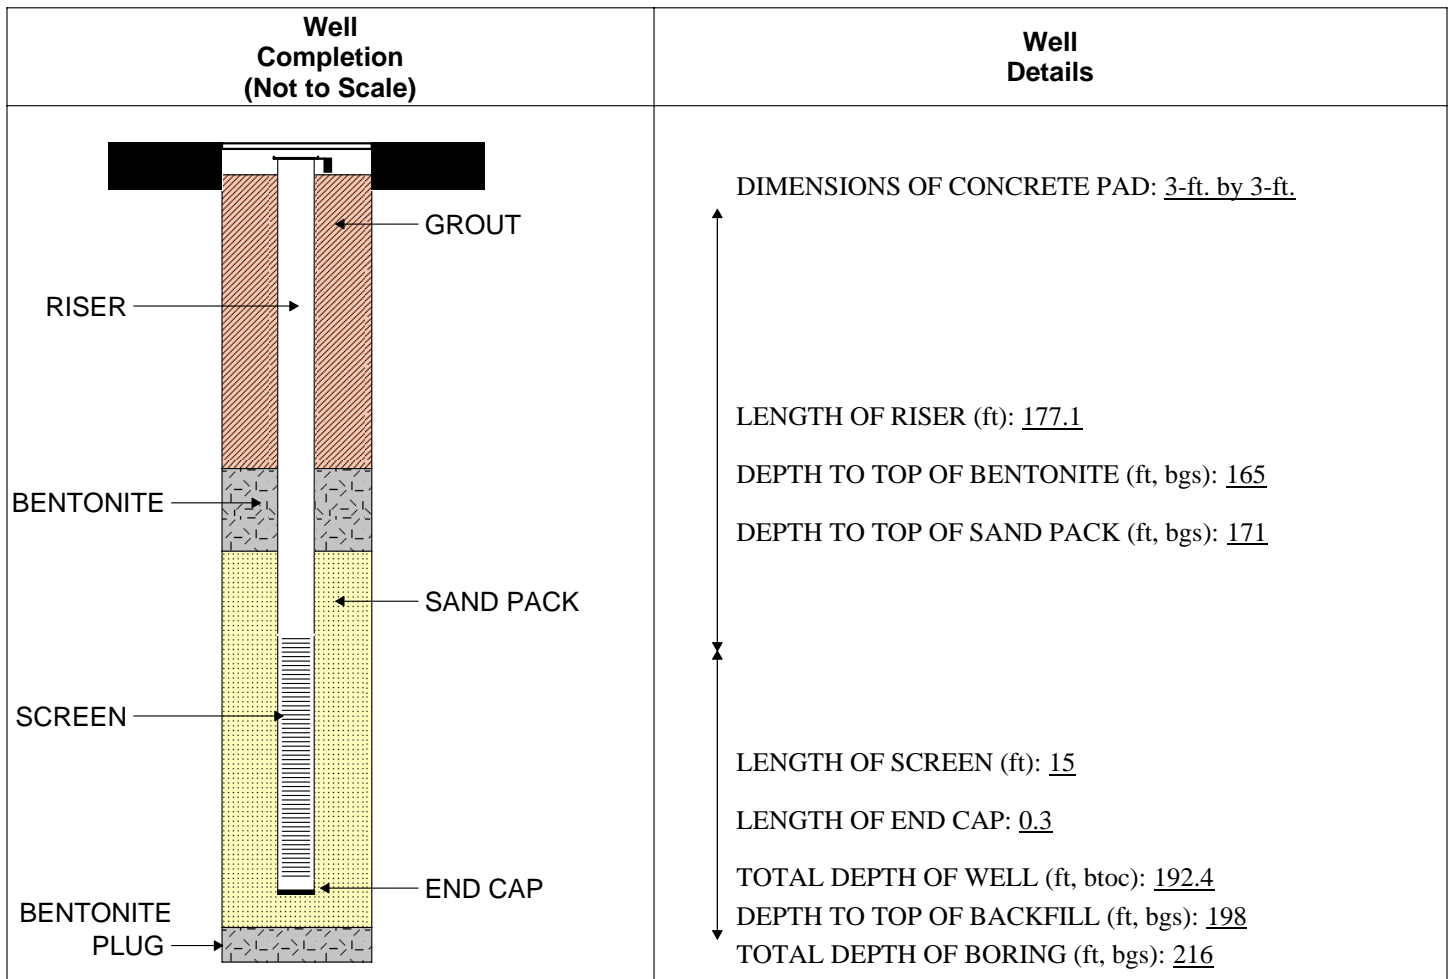

Prepared by: **WTR**

Date: **5/16/2007**

Checked by: **KMS**

Date: **5/16/2007**
