


## **Monitoring Well / Piezometer Completion Diagram**

## Flush Mount

Northing Memphis Depot **Project Number** 334469.SA.HS 280918.68 **Project Name Project Location** Memphis, Tennessee Start Date / Time 9/13/2007 **Easting** 802082.45 Well / Piezometer ID MW-238 End Date / Time 9/18/2007

<b>Ground Surface Elevation</b>	300.70	Static Water Level (ft btoc)	140.02	
Top of Casing Elevation	300.45	Measured On	9/24/2007	
Concrete Pad		Filter Pack Type	20 / 40	
Dimensions	3 x 3 ft	Manufacturer	Southern Filter Media	
Drain Tube	N	Amount Sand Used	4 X 50-lb bag(s)	
Well Casing		Bentonite Type	3/8" Chips / Bentonite Powder (Gel)	
Diameter	2"	Manufacturer	DSI SHUR-PLUG / DSI PURE-GEL	
Material	Schedule 40 PVC	Amount Bentonite Below Screen	N/A	
Material	Stainless Steel (0-20 ft bgs)	Amount Bentonite Used (Seal)	1.5 X 50-lb bag(s)	
Screen	· · · · · · · · · · · · · · · · · · ·	-		
Diameter	2"	Cement Type	Portland Type I	
Material	Schedule 40 PVC	Manufacturer	Ash Grove	
Slot Size	0.01	Amount Cement Used (Grout)	12 X 92.6-lb bag(s)	
		Density of Grout	12.6 lbs/gal	
Permanent Casing				
Diameter	6"	Cement Type (Permanent Casing)	Portland Type I	
Material	Schedule 80 PVC	Manufacturer	Ash Grove	
		Amount Cement Used (Grout)	15 X 92.6-lb bag(s)	
		Density of Grout	12.5 lbs/gal	
Drilling Technique	Rotosonic (R <sub>1</sub> ) / Rotosonic (R <sub>2</sub> )			
Auger/Bit Size and Type	(R <sub>1</sub> ) 4" Core / 6"; 9.25" Casing	_		
Auger/Bit Size and Type	(R <sub>2</sub> ) 3" Core / 5.75" Casing	Drilling Contractor	Boart Longyear	
Borehole Diameter	(R <sub>1</sub> ) 9.5" / (R <sub>2</sub> ) 6"	CH2M HILL Field Representative	Derek Miller	

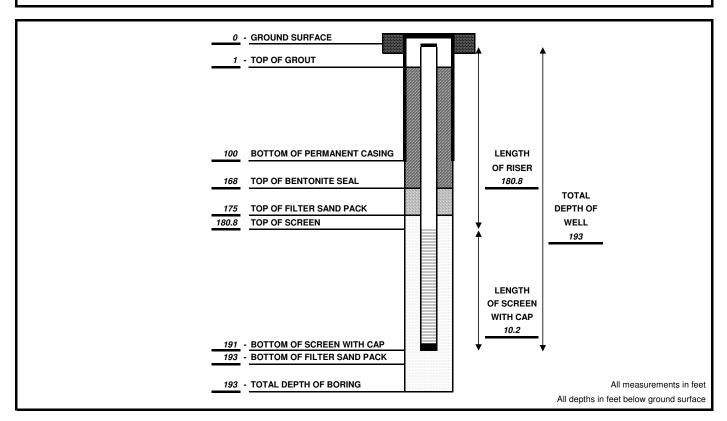

	DRILLER:	T. Overcash	INSPECTOR:	Derek Miller	
QA / QC			CHECKED BY:	: D. Nelson	DATE: 10/20/2007
	DISCREPANCIES:				
