



WELL INSTALLATION DIAGRAM

WELL NO.: MW-265

PROJECT: SRI Phase I
PROJECT NUMBER: 235772
SITE LOCATION: DDMT MI
PROJECT MANAGER: T. Holmes
FIELD STAFF: S. Gillet
DATE COMPLETED: 5/12/2015
WELL LOCATION: SW corner of Bldg 429 in parking area near Kotick St.


NORTHING: 278111.58
EASTING: 804709.99
GROUND SURFACE ELEVATION (ft, msl): 305.61
TOP OF CASING ELEVATION (ft, msl): 305.15
TOP OF SCREEN ELEVATION (ft, msl): 219.4

DRILLING CO.: Cascade Drilling, L.P.
DRILLING METHOD: Sonic
BOREHOLE DIAMETER (in): 6
SURFACE COMPLETION: Flush Mount
BOLLARDS: No
WELL DIAMETER (in): 2
TYPE OF SCREEN/RISER MATERIAL: Sch. 40 PVC
SLOT SIZE OF SCREEN: 0.010-in.

TYPE OF FILTER PACK: Silica Sand
GRADATION OF FILTER PACK: 8/16 Sand
QUANTITY OF FILTER PACK: 5 - 50lb bags
TYPE OF BENTONITE IN SEAL: EnviroPlug Med. Chips
QUANTITY OF BENTONITE IN SEAL: 1-50lb bag
TYPE OF GROUT: Type I/II cement with 4% bentonite
QUANTITY OF GROUT: 95 gallons
DEVELOPMENT METHOD: Surge & Pump (M.Monsoon)
DATE DEVELOPED: 5/14/15
DEPTH TO WATER (ft.btoc): 75.68

NOTES: Boring backfilled with bentonite from 97 to 107 ft, bgs prior to well installation.
150 gallons water used during drilling; 275 gallons removed during development. Depth to water measured on 5/19/15.

Well Completion (Not to Scale)

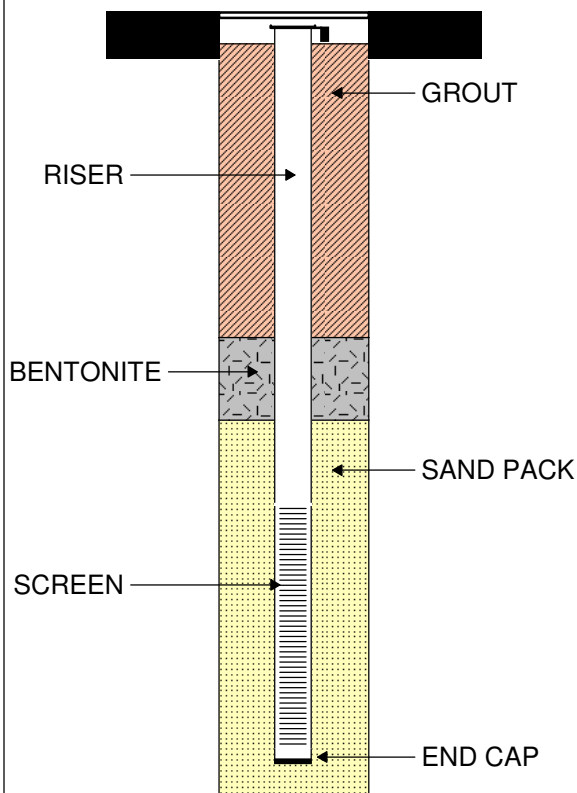

Well Details

DIMENSIONS OF CONCRETE PAD: 3ft. X 3ft.

LENGTH OF RISER (ft): 85.8

DEPTH TO TOP OF BENTONITE (ft, bgs): 76.3

DEPTH TO TOP OF SAND PACK (ft, bgs): 81.3

LENGTH OF SCREEN (ft): 10

LENGTH OF END CAP: 0.2 ft.

TOTAL DEPTH OF WELL (ft, btoc): 96.0

TOTAL DEPTH OF BORING (ft, bgs): 107

Prepared by: WTR

Date: 8/13/15

Checked by: TCH

Date: 8/13/15
