



WELL INSTALLATION DIAGRAM

WELL NO.: MW-287


PROJECT: SRI Phase 3
PROJECT NUMBER: 10058697
SITE LOCATION: DDMT, Main Installation
PROJECT MANAGER: T. Holmes
FIELD STAFF: C. Mokri
DATE COMPLETED: 6/16/2018
WELL LOCATION: W building 529

NORTHING: 278236.47
EASTING: 803971.22
GROUND SURFACE ELEVATION (ft, NAVD): 305.01
TOP OF CASING ELEVATION (ft, NAVD): 304.67
TOP OF SCREEN ELEVATION (ft, NAVD): 220.8

DRILLING CO.: Cascade Drilling, L.P.
DRILLING METHOD: Sonic
BOREHOLE DIAMETER (in): 6
SURFACE COMPLETION: Flush Mount
BOLLARDS: No
WELL DIAMETER (in): 2
TYPE OF SCREEN/RISER MATERIAL: Sch. 40 PVC
SLOT SIZE OF SCREEN: 0.010-in.

TYPE OF FILTER PACK: Silica Sand
GRADATION OF FILTER PACK: 15/18 Red Flint S&G
QUANTITY OF FILTER PACK: 9 - 50lb bags
TYPE OF BENTONITE IN SEAL: Holeplug 3/8" Chips
QUANTITY OF BENTONITE IN SEAL: 1 -50lb bag
TYPE OF GROUT: Type I/II cement with 4% bentonite
QUANTITY OF GROUT: 100 gallons
DEVELOPMENT METHOD: Surge&Pump
DATE DEVELOPED: 7/16/2018
DEPTH TO WATER (ft.btoc): 79.76

NOTES: No water used during drilling; 48 gallons removed during development. Depth to water measured on 08/11/18.

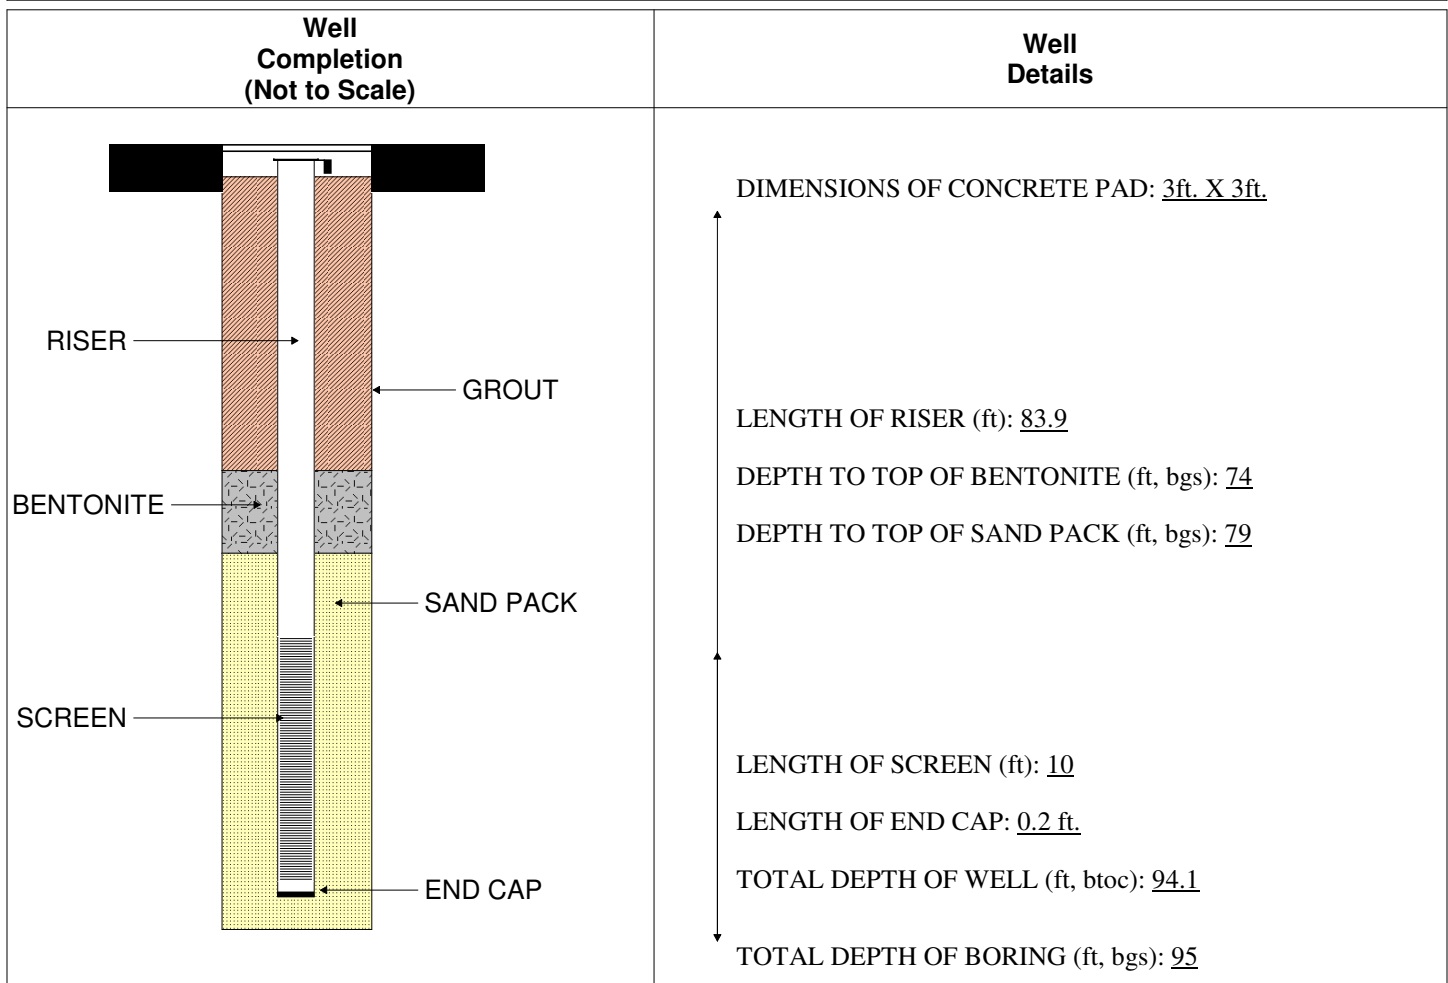

Prepared by: WTR Date Prepared: 8/30/2018

Checked by: TCH

Date Checked: 9/28/2018
