

CHM HILL MONITORING WELL CONSTRUCTION LOG

Standard Flush Mount

Installation DDMT

Site NW of Dunn Field

Project Number 11363φ. φ1.22

Drilling Contractor Boart Longyear

Built By Boart Longyear

Well Number MW-40 (0)

Client/Project DDMT Groundwater Invest.


Starting date 10 JAN 96 time 1025

Completion date 11 JAN 96 time 1500

Well Coordinates _____

Elevation _____
Height _____
GS Elevation _____

DEPTH BGS

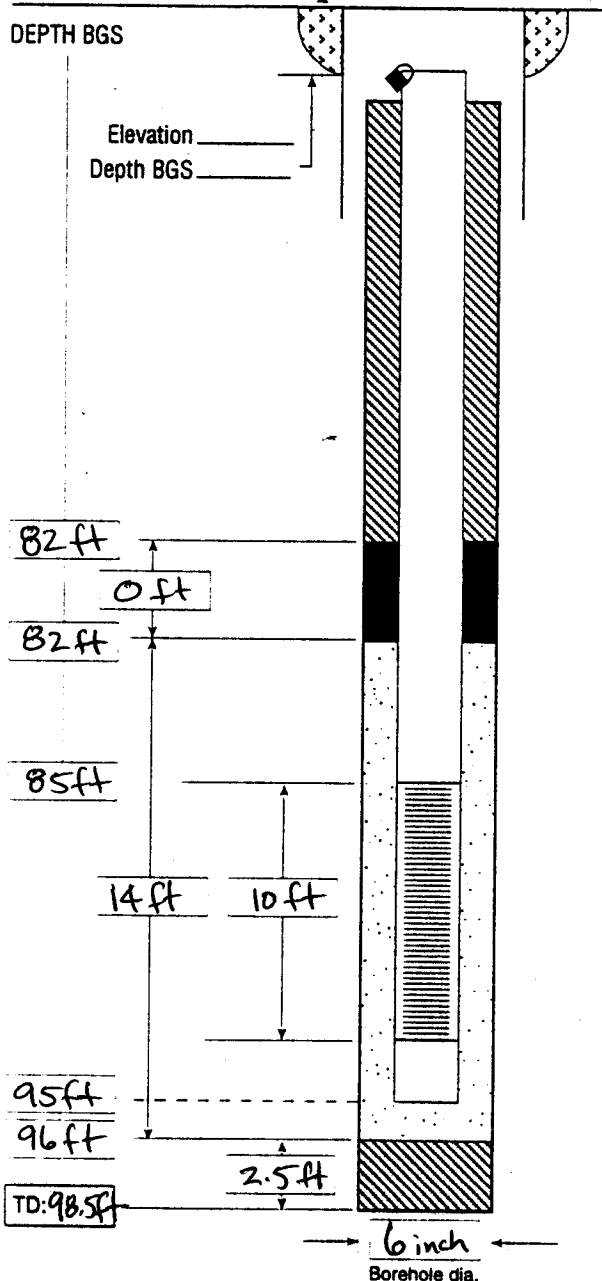

PROTECTIVE CSG

Material / Type Steel
Diameter 4 inch Water Tight Seal ☒ (Y / N)
Depth BGS _____ Weep Hole (Y / N)

SURFACE PAD

Composition & Size Concrete 3ft x 3ft

RISER PIPE

Type Schedule 40 PVC
Diameter 2 inch
Total Length (TOC to TOS) 85 ft

GROUT

Composition & Proportions High Solids (30%)
Bentonite Clay - Pure Gold
Tremied ☒ (Y / N)
Interval BGS 0 ft to 82 ft

CENTRALIZERS (Y / N)

Depth(s) BGS _____

SEAL

Type N/A
Source _____
Hydration Time _____ Volume of Fluid Added _____
Tremied (Y / N)

FILTER PACK

Type Sand 20/40
Amount Used 6 50# bags
Tremied (Y / N)
Source The Morie Company
Gr. Size Dist. Grade 00N

SCREEN

Type Schedule 40 PVC
Diameter 2 inch
Slot Size & Type 0.010 inch
Interval BGS 85 ft to 95 ft

BACKFILL PLUG

Material Bentonite Pellets
Hydration Time _____
Tremied (Y / N)
