

CHM HILL MONITORING WELL CONSTRUCTION LOG

Standard Flush Mount

Installation DDMT

Site West of Dunn Field

Project Number 11363Φ. Φ1. ZZ

Drilling Contractor Baart Longyear

Built By Baart Longyear

Well Number MW-44 (m)

Client/Project DDMT Groundwater Inv.

Starting date 15 JAN 96 time 0945


*Temporary Completion date 16 JAN 96 time 1400

Well Coordinates _____

Elevation _____
Height _____
GS Elevation _____

DEPTH BGS

Elevation _____
Depth BGS _____

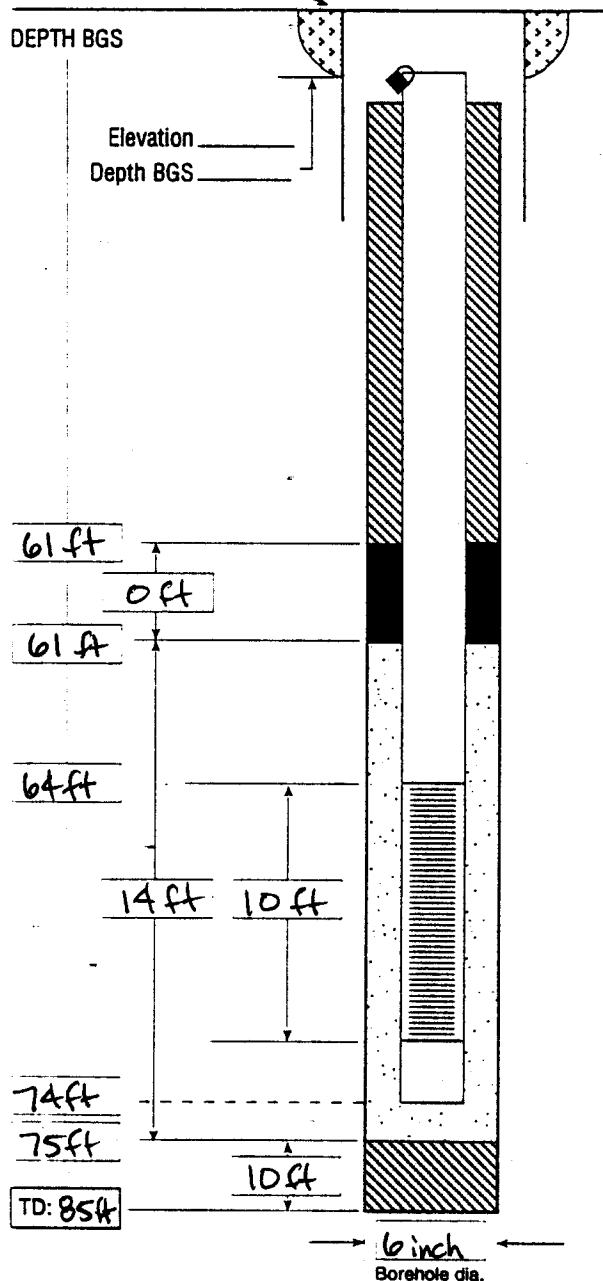

PROTECTIVE CSG

Material / Type Steel
Diameter 4 inch Water Tight Seal (Y) / N)
Depth BGS _____ Weep Hole (Y / N)

SURFACE PAD

Composition & Size _____

RISER PIPE

Type Schedule 40 PVC
Diameter 2 inch
Total Length (TOC to TOS) 64 ft

GROUT

Composition & Proportions High Solids (30%)
Bentonite Clay - Pure Gold
Tremied (Y / N)
Interval BGS 0 ft to 61 ft

CENTRALIZERS (Y (N))

Depth(s) BGS _____

SEAL

Type N/A
Source _____
Hydration Time _____ Volume of Fluid Added _____
Tremied (Y / N)

FILTER PACK

Type 20/40 Silica Sand
Amount Used 4 50 lb bags
Tremied (Y (N))
Source The Morie Company
Gr. Size Dist. Grade 00N

SCREEN

Type Schedule 40 PVC
Diameter 2 inch
Slot Size & Type 0.010 inch
Interval BGS 64 ft to 74 ft

BACKFILL PLUG

Material Bentonite Pellets
Hydration Time _____
Tremied (Y / (N))
