

CHM HILL MONITORING WELL CONSTRUCTION LOG

Standard Flush Mount

Installation DDMT

Site Dunn Field

Project Number 113634.01.22

Drilling Contractor Boart Longyear

Built By Boart Longyear

Well Number MW-46 (B)

Client/Project DDMT Groundwater Invest.


Starting date 22 JAN 96 time 1048

Completion date 27 JAN 96 time

Well Coordinates

Elevation
Height
GS Elevation

DEPTH BGS

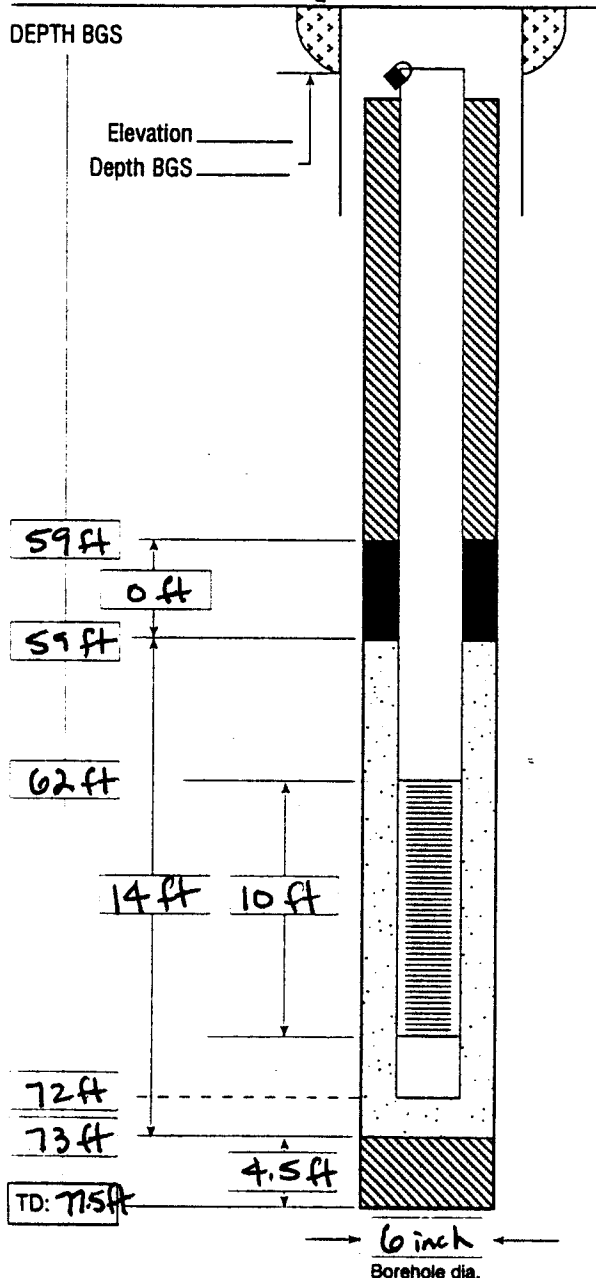

PROTECTIVE CSG

Material / Type Steel
Diameter 4 inch Water Tight Seal (Y) (N)
Depth BGS Weep Hole (Y / N)

SURFACE PAD

Composition & Size

RISER PIPE

Type Schedule 40 PVC
Diameter 2 inch
Total Length (TOC to TOS) 62 feet

GROUT

Composition & Proportions High Solids (30%)
Bentonite Clay - Pure Gold
Tremied (Y) (N)
Interval BGS 0 ft to 59 ft

CENTRALIZERS (Y (N))

Depth(s) BGS

SEAL

Type N/A
Source
Hydration Time Volume of Fluid Added
Tremied (Y / N)

FILTER PACK

Type 20/40 Silica Sand
Amount Used 4 50# bags
Tremied (Y) (N)
Source The Monie Company
Gr. Size Dist. Grade 00N

SCREEN

Type Schedule 40 PVC
Diameter 2 inch
Slot Size & Type 0.010 inch
Interval BGS 62 ft to 72 ft

BACKFILL PLUG

Material Bentonite Pellets
Hydration Time
Tremied (Y) (N)
