

CH2M HILL MONITORING WELL CONSTRUCTION LOG

Standard Flush Mount

Installation DDMT

Site Dunn Field

Project Number 11363φ. φ1. 22

Drilling Contractor Boart Longyear

Built By Boart Longyear


Well Number MW-49 (D)

Client/Project DDMT Groundwater Inv.

Starting date 25 JAN 96 time 1010

Completion date 27 JAN 96 time

Well Coordinates

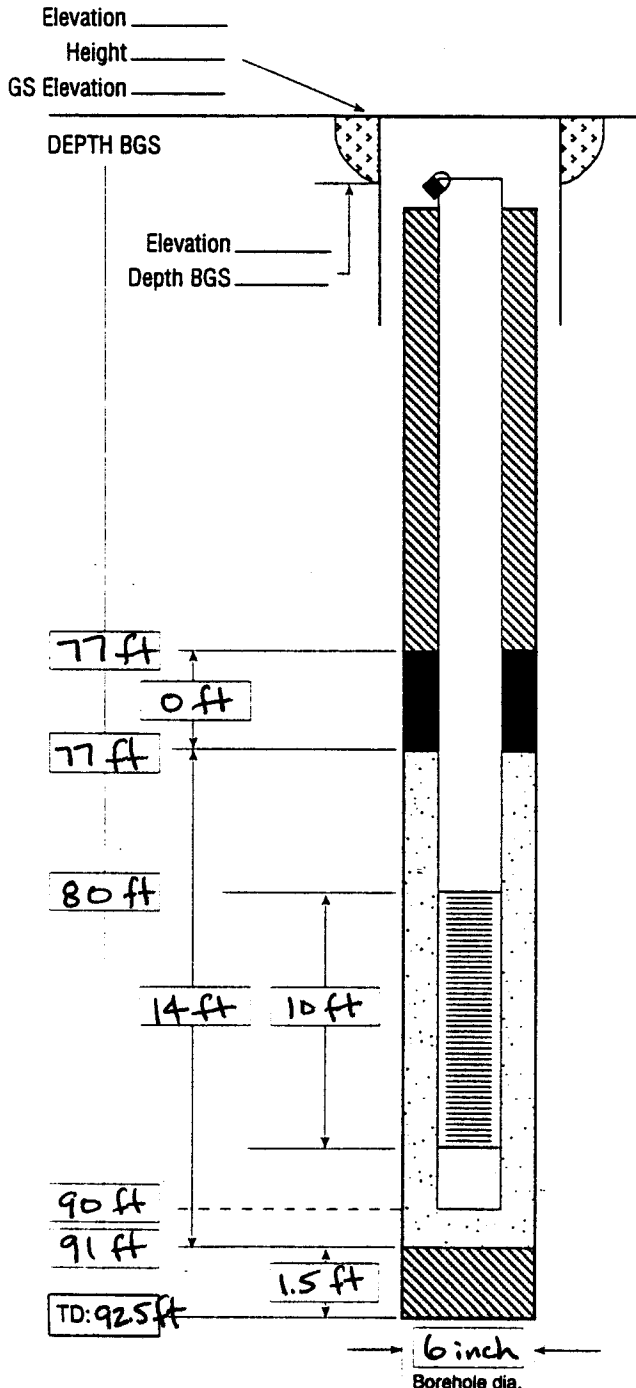

PROTECTIVE CSG

Material / Type Steel

Diameter 4 inch Water Tight Seal ☒ (Y / N)

Depth BGS _____ Weep Hole (Y / N)

SURFACE PAD

Composition & Size _____

RISER PIPE

Type Schedule 40 PVC

Diameter 2 inch

Total Length (TOC to TOS) 80 feet

GROUT

Composition & Proportions High Solids (30%)

Bentonite Clay - Pure Gold

Tremied ☒ (Y / N)

Interval BGS 0 ft to 77 ft

CENTRALIZERS (Y / ☒ N)

Depth(s) BGS _____

SEAL

Type N/A

Source _____

Hydration Time _____ Volume of Fluid Added _____

Tremied (Y / N)

FILTER PACK

Type 20/40 Silica Sand

Amount Used 4 50# bags

Tremied ☒ (Y / N)

Source The Morie Company

Gr. Size Dist. Grade 00N

SCREEN

Type Schedule 40 PVC

Diameter 2 inch

Slot Size & Type 0.010 inch

Interval BGS 80 ft to 90 ft

BACKFILL PLUG

Material Bentonite Pellets

Hydration Time _____

Tremied (Y / ☒ N)
