

CHM HILL MONITORING WELL CONSTRUCTION LOG

Standard Flush Mount

Installation DDMT

Site North of Main Installation

Project Number 113630. 01. 22

Drilling Contractor Boart Longyear

Built By Boart Longyear


Well Number MW-53 (E)

Client/Project DDMT GW Invest.

Starting date 02 FEB 96 time 0455

Completion date 03 FEB 96 time 1245

Well Coordinates _____

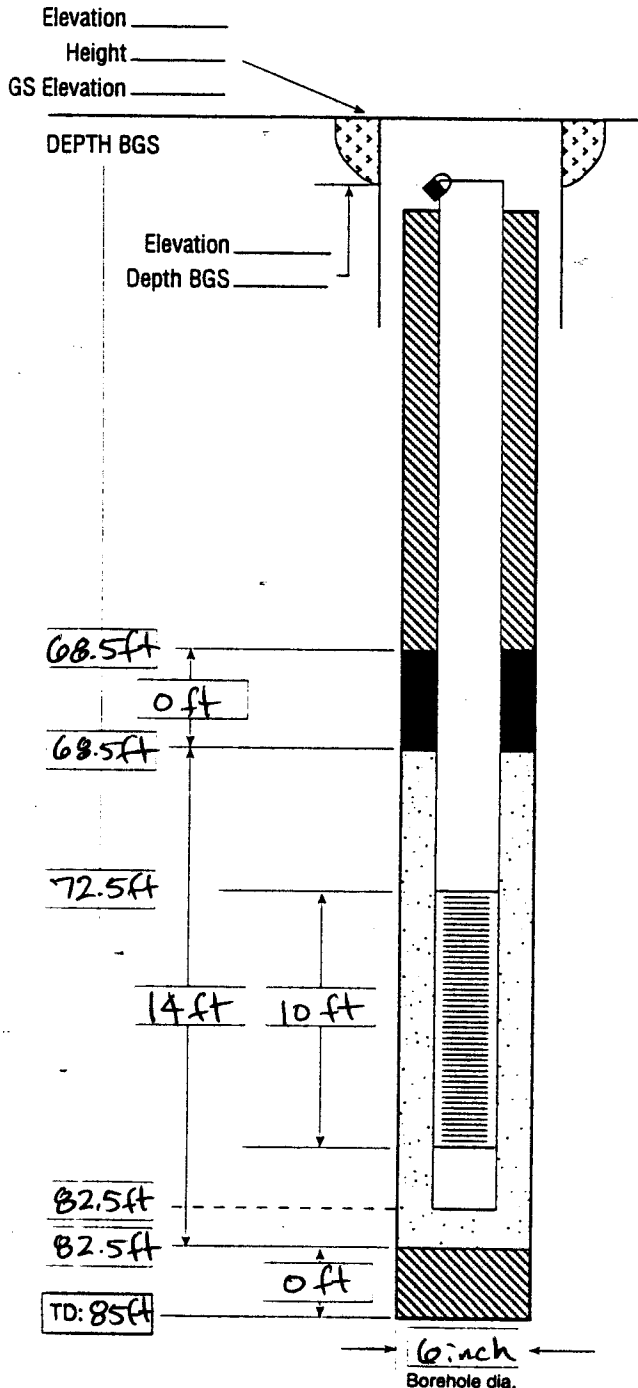

PROTECTIVE CSG

Material / Type _____

Diameter _____ Water Tight Seal (Y / N)

Depth BGS _____ Weep Hole (Y / N)

SURFACE PAD

Composition & Size _____

RISER PIPE

Type Schedule 40 PVC

Diameter 2 inch

Total Length (TOC to TOS) _____

GROUT

Composition & Proportions High Solids (30%)

Bentonite Clay - PureGold

Tremied (Y / N)

Interval BGS _____

CENTRALIZERS (Y / N)

Depth(s) BGS _____

SEAL

Type N/A

Source _____

Hydration Time _____ Volume of Fluid Added _____

Tremied (Y / N)

FILTER PACK

Type 20/40 Silica Sand

Amount Used 5 50# bags

Tremied (Y / N)

Source The Morie Company

Gr. Size Dist. Grade 00N

SCREEN

Type Schedule 40 PVC

Diameter 2 inch

Slot Size & Type 0.010 inch

Interval BGS _____

BACKFILL PLUG

Material N/A

Hydration Time _____

Tremied (Y / N)
