



WELL INSTALLATION DIAGRAM

WELL NO.: PMW101-04B

PROJECT: DDMT - Main Installation Remedial Action

PROJECT NUMBER: 3202-016

SITE LOCATION: TTA-1

e2M PROJECT MANAGER: T. Holmes

e2M FIELD STAFF: E. Van Schaik

DATE COMPLETED: 6/6/2006

WELL LOCATION:

NORTHING: 276296.396

EASTING: 801186.855

GROUND SURFACE ELEVATION (msl): 291.75

TOP OF CASING ELEVATION (msl): 291.47

TOP OF SCREEN ELEVATION (msl): 192.91

DRILLING CO.: Prosonic

DRILLING METHOD: Sonic

BOREHOLE DIAMETER (in): 6

SURFACE COMPLETION: Flush Mount

BOLLARDS: No

WELL DIAMETER (in): 2

TYPE OF SCREEN/RISER MATERIAL: PVC Schedule 40

SLOT SIZE OF SCREEN: 0.010

TYPE OF FILTER PACK: Sand

GRADATION OF FILTER PACK: 10-20

QUANTITY OF FILTER PACK: 12-50lb. Bags

TYPE OF BENTONITE IN SEAL: 3/8" Shur Plug Chips

QUANTITY OF BENTONITE IN SEAL: 1-50lb. Bag

TYPE OF GROUT: Portland Type I


QUANTITY OF GROUT: 17-94lb. Bags

DEVELOPMENT METHOD: Grundfos RediFlow II

DATE DEVELOPED: 6/22/2006

DEPTH TO WATER (ft.btoc): 89.5

NOTES:

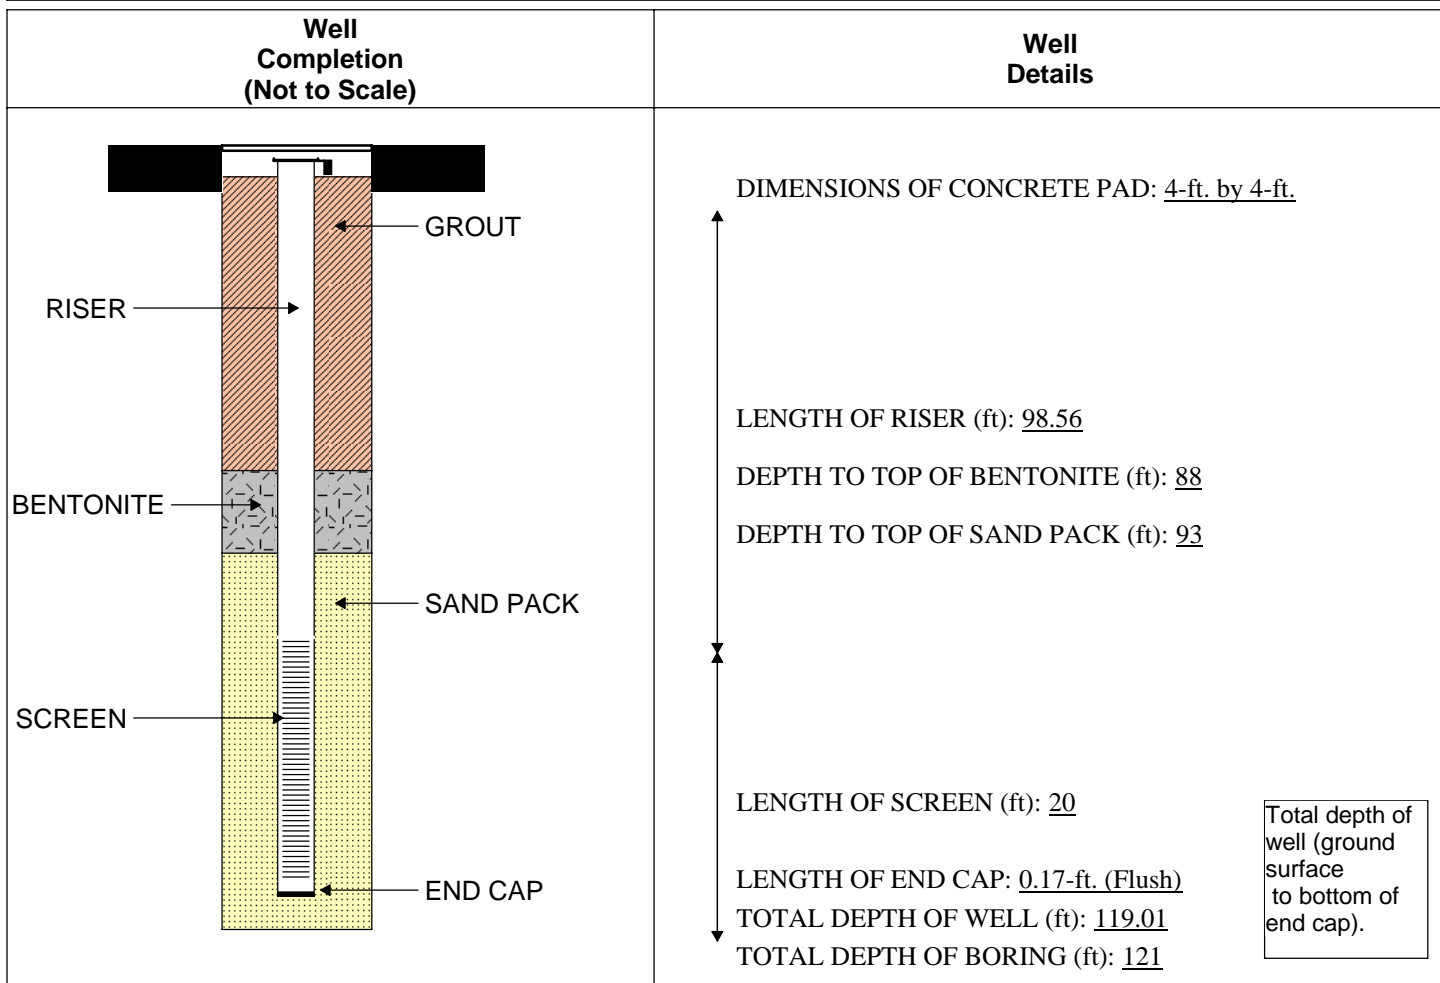

Prepared by: WTR

Date: 12/13/06

Checked by: KMS

Date: 12/13/06
