



WELL INSTALLATION DIAGRAM

WELL NO.: PMW101-08A

PROJECT: DDMT - Main Installation Remedial Action

PROJECT NUMBER: 3202-016

SITE LOCATION: TTA-1

e2M PROJECT MANAGER: T. Holmes

e2M FIELD STAFF: E. Van Schaik

DATE COMPLETED: 7/9/2006

WELL LOCATION:

NORTHING: 276070.278

EASTING: 801119.022

GROUND SURFACE ELEVATION (msl): 293.3

TOP OF CASING ELEVATION (msl): 293.01

TOP OF SCREEN ELEVATION (msl): 173.26

DRILLING CO.: Prosonic

DRILLING METHOD: Sonic

BOREHOLE DIAMETER (in): 6

SURFACE COMPLETION: Flush Mount

BOLLARDS: No

WELL DIAMETER (in): 2

TYPE OF SCREEN/RISER MATERIAL: PVC Schedule 40

SLOT SIZE OF SCREEN: 0.010

TYPE OF FILTER PACK: Sand

GRADATION OF FILTER PACK: 10-20

QUANTITY OF FILTER PACK: 7-50lb. Bags

TYPE OF BENTONITE IN SEAL: 3/8" Shur Plug Chips

QUANTITY OF BENTONITE IN SEAL: 1-50lb. Bag

TYPE OF GROUT: Portland Type I


QUANTITY OF GROUT: 18-94lb. Bags

DEVELOPMENT METHOD: Grundfos RediFlow II

DATE DEVELOPED: 8/2/2006

DEPTH TO WATER (ft.btoc): 90.8

NOTES:

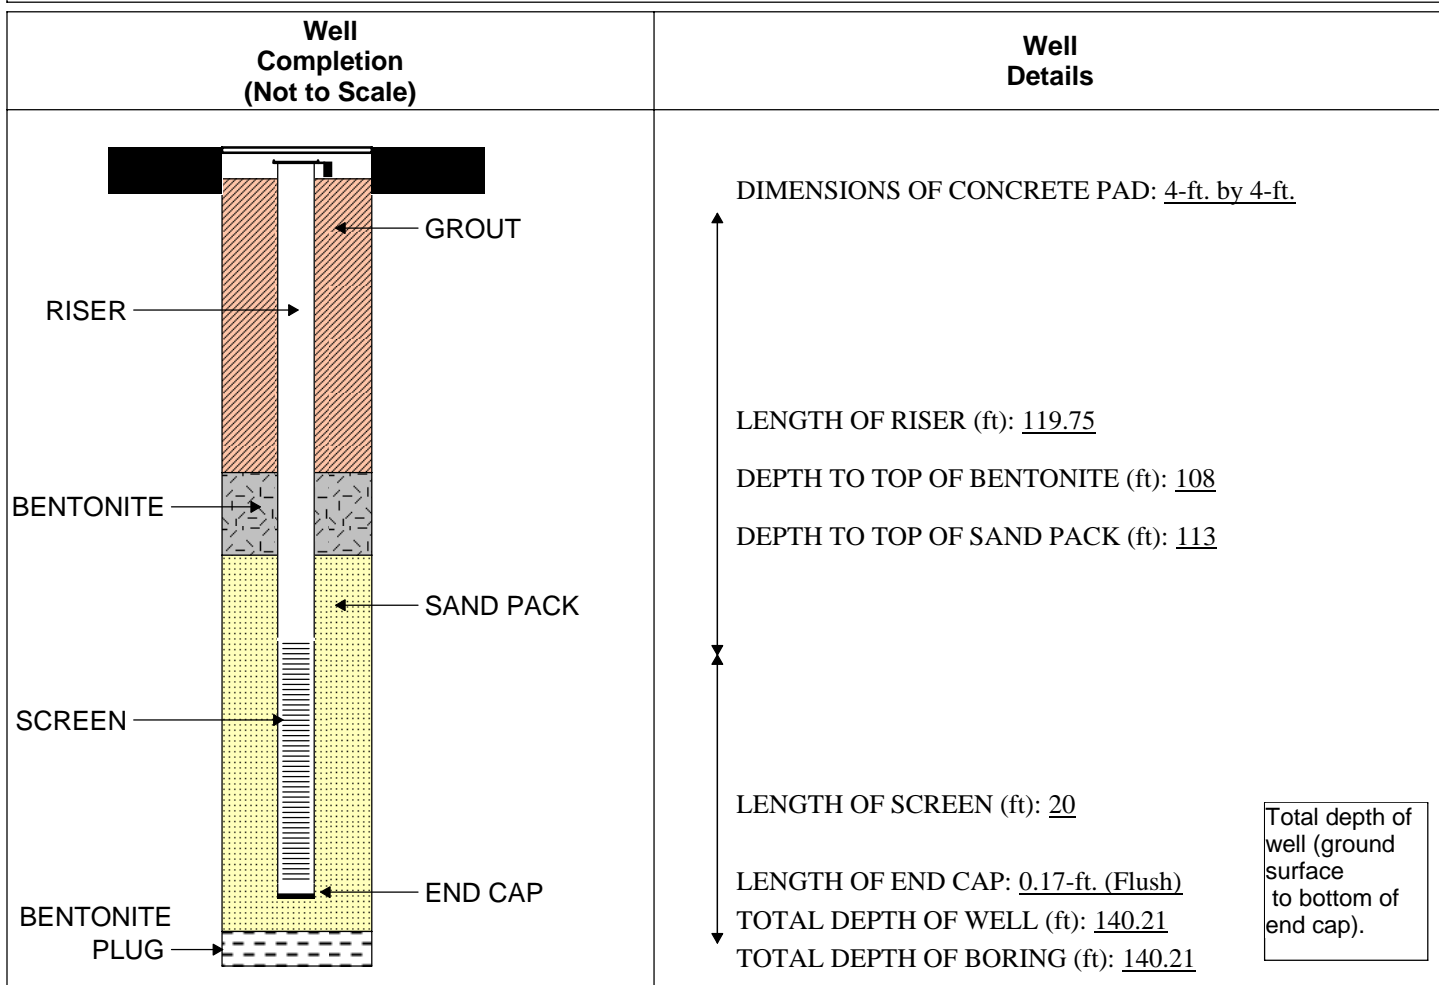

Prepared by: WTR

Date: 12/13/06

Checked by: KMS

Date: 12/13/06
