




PROJECT NUMBER 170039	WELL NUMBER MW-106	SHEET 1 OF 1
WELL COMPLETION DIAGRAM		

PROJECT : EBT Treatability Study	LOCATION : Memphis Depot
DRILLING CONTRACTOR : Boart Longyear	
DRILLING METHOD AND EQUIPMENT USED : Rotasonic rig (4 inch sample casing / 6 inch outer casing)	
WATER LEVELS :	START : 04/17/2002 END: 04/17/2002 LOGGER : Mike Karafa

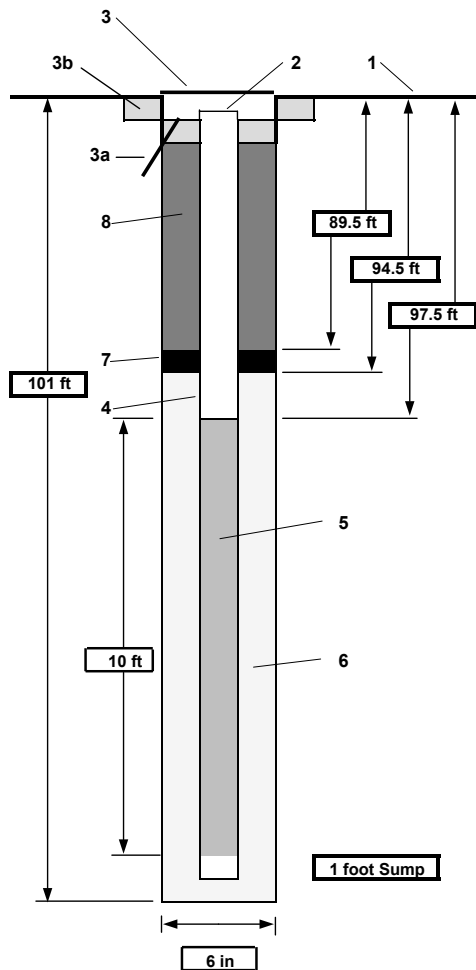

Note: Diagram not to scale.

1- Ground elevation at well	feet MSL
2- Top of casing elevation	feet MSL
3- Wellhead protection cover type	Flush-mount wellhead pad
a) drain tube?	No
b) concrete pad dimensions	3 by 3 feet
4- Dia./type of well casing	2 inch Schedule 40 PVC
5- Type/slot size of screen	2 inch 10-slot Schedule 40 PVC
6- Type screen filter	Sand, DSI #2
a) Quantity used	bags
7- Type of seal	Bentonite pellets, DSI Shur-plug 3/8"
a) Quantity used	bags
8- Grout	90% grout / 10% bentonite powder
a) Grout mix used	
b) Method of placement	Tremmie Method
c) Vol. of well casing grout	
Development method	Surge and develop with stainless steel bailer to remove sediment. Submersible pump.
Development time	8.3 hour
Estimated purge volume	42.5 gallons
Comments	Total Depth (BGS) = 100 feet
Final field parameters collected during well development (/ /):	
pH =	
conductivity = mS/cm	
temperature = °C	
Dissolved Oxygen = mg/l	
Turbidity = NTU	
